K Ravish Rao
PES1UG24AM127

Software Engineering Laboratory

SE LAB 02

Agile Backlog Creation & Sprint Simulation in Jira

Name: K Ravish Rao
SRN: PES1UG24AM127

Jira Project: SE Lab 02 – Agile Sprint Simulation
Board: SLOASS

1. Objective

To create an Agile backlog in Jira, organize work under an Epic, assign Story Points, plan and execute two sprints, move work through the Scrum workflow, and review the sprint burndown report.

2. Project and Backlog Structure

The Jira board used for the exercise is the SLOASS board under the project “SE Lab 02 – Agile Sprint Simulation”. The backlog contains one Epic and five User Stories.

Issue	User Story	Priority	Story Points
SLOASS-2	Open Completed Mock Interview Session	High	3
SLOASS-3	Access Post-Interview Scorecard	High	3
SLOASS-4	Record Structured Performance Ratings	High	5
SLOASS-5	Record Qualitative Interview Feedback	Medium	5
SLOASS-6	Save and Submit Interview Scorecard	High	3

Epic: Post-Interview Scorecard Recording (SLOASS-1)

Total backlog estimate: 19 Story Points.

3. Backlog with User Stories and Story Points

The backlog view shows all five User Stories grouped under the Post-Interview Scorecard Recording Epic. Story Point estimates are 3, 3, 5, 5 and 3, giving a total of 19 points.

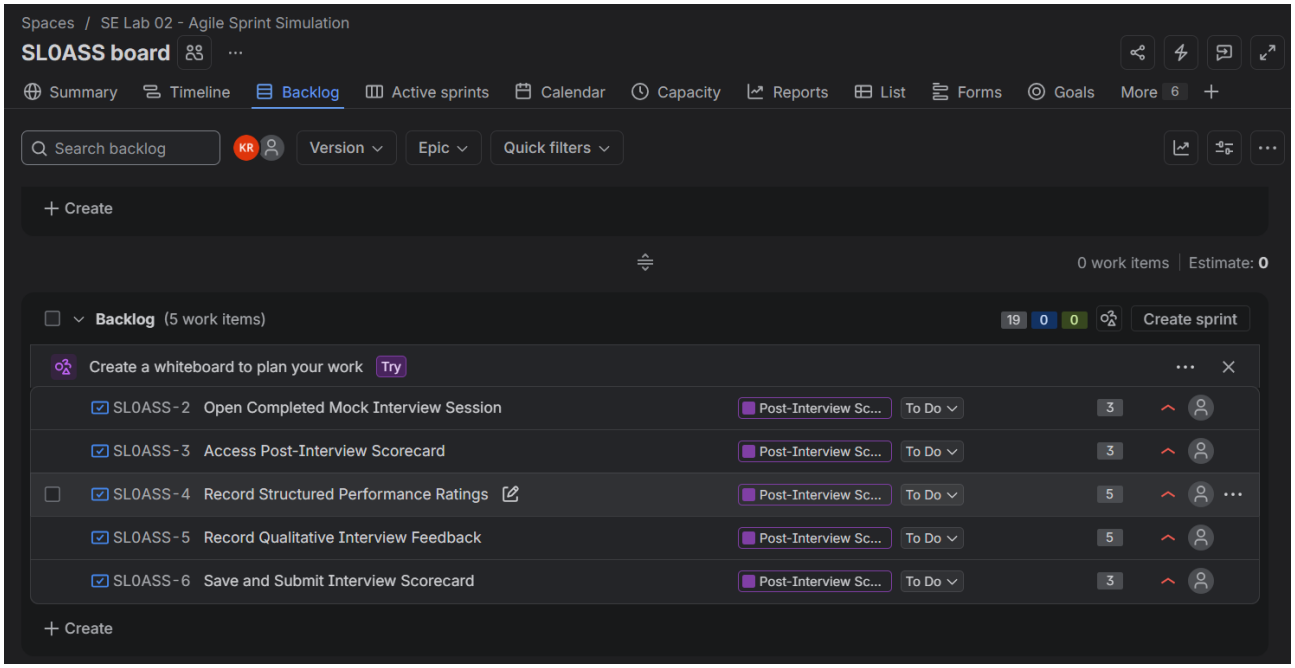


Figure 1. Jira backlog showing the five User Stories, Epic relationship, status and Story Points.

4. Sprint 1 Planning and Execution

Sprint 1 was planned with three User Stories: SLOASS-2, SLOASS-3 and SLOASS-4. Their estimates were 3, 3 and 5 Story Points respectively, giving Sprint 1 a planned capacity of 11 points.

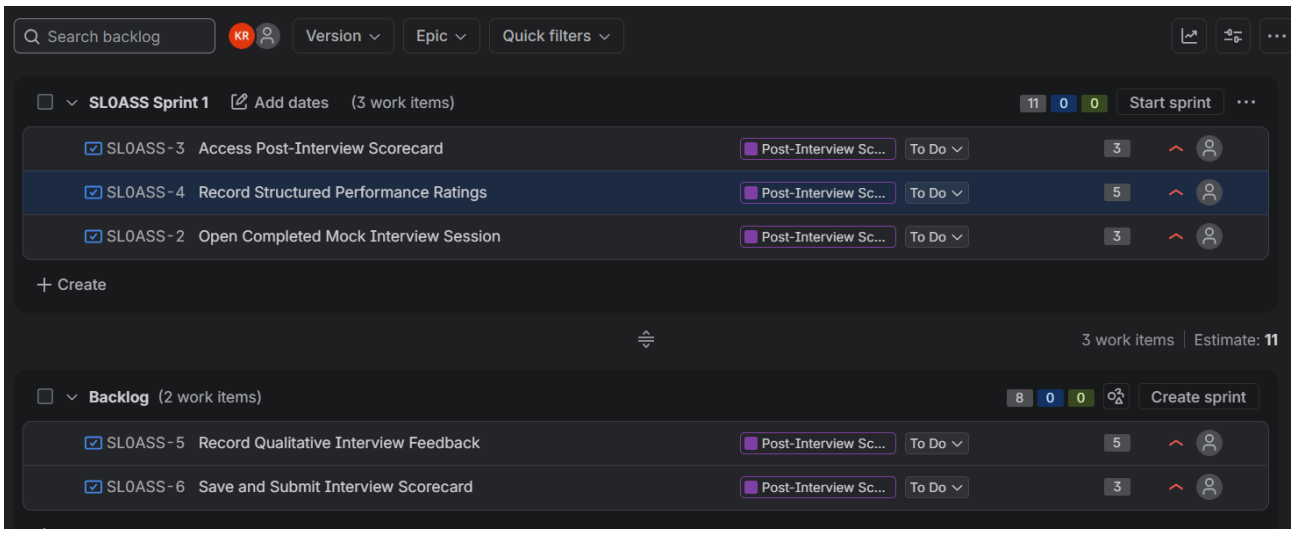


Figure 2. Sprint 1 planning view with 3 work items and an 11-point estimate.

After the sprint was started, all three Sprint 1 stories were initially visible in the To Do column.

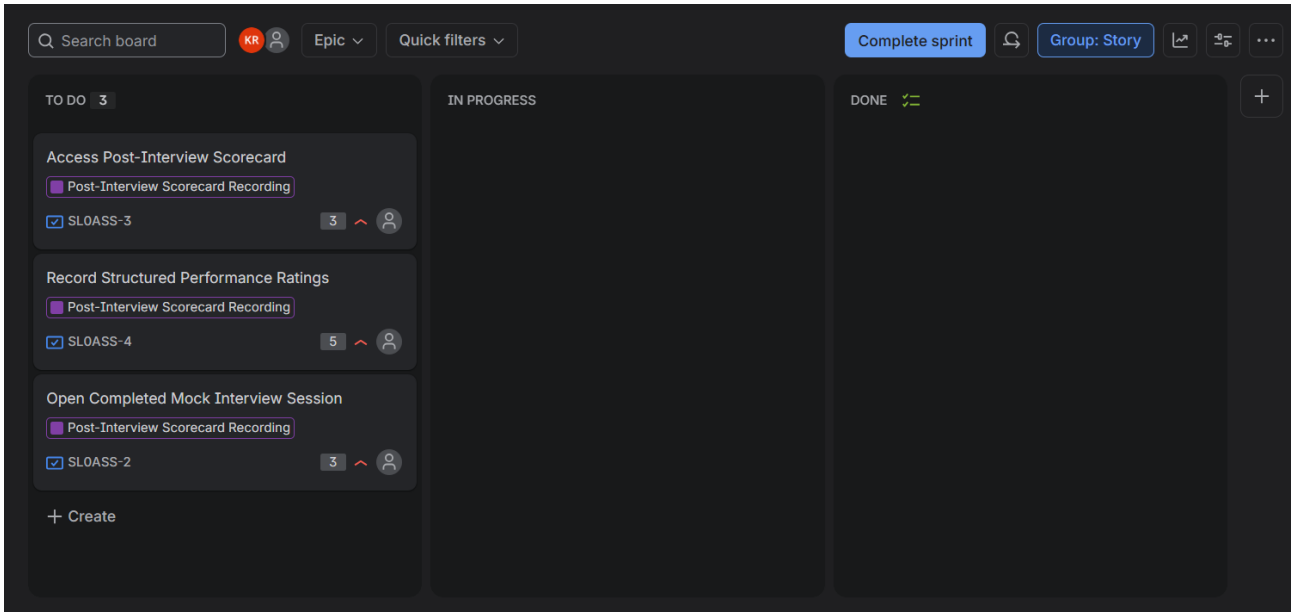


Figure 3. Sprint 1 Active Sprint view at the start of execution.

The three stories were then progressed through the Scrum workflow and completed.

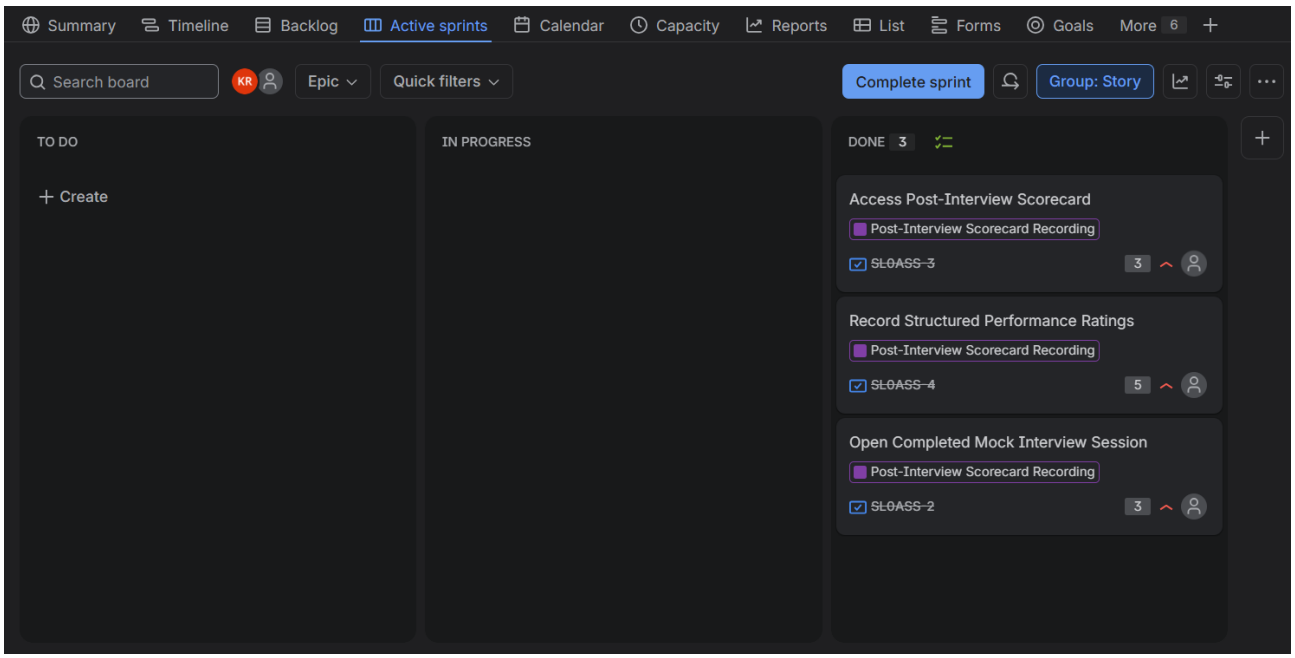


Figure 4. Sprint 1 completed state with all three stories in Done.

5. Sprint 2 Planning and Execution

The remaining two User Stories were assigned to Sprint 2: SLOASS-5 (5 points) and SLOASS-6 (3 points). Sprint 2 therefore contained 8 Story Points.

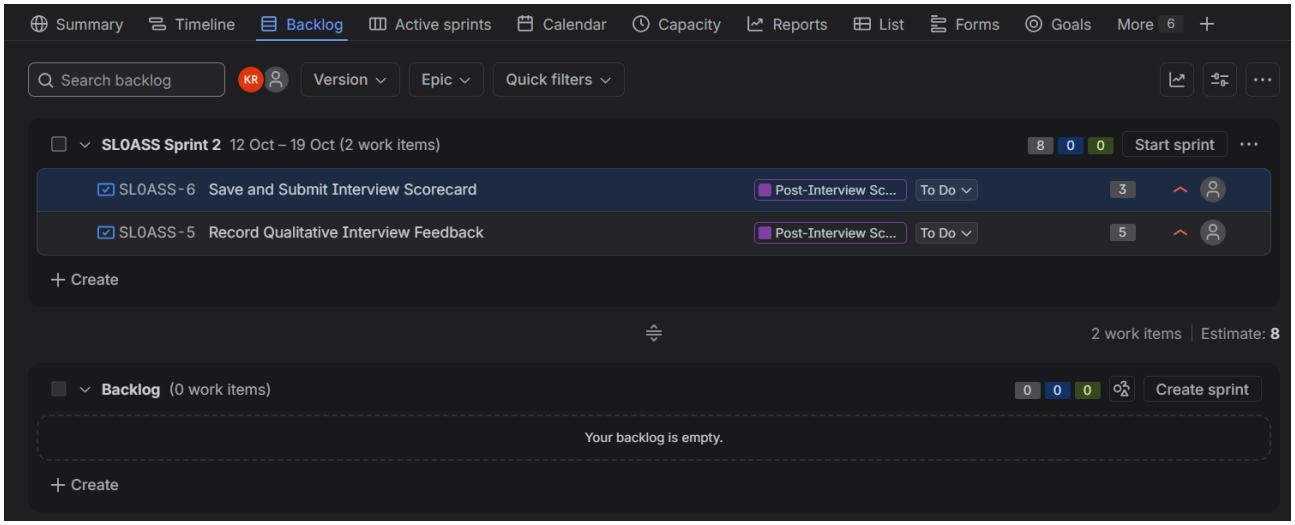


Figure 5. Sprint 2 planning view with 2 work items and an 8-point estimate.

Sprint 2 was started with both stories in the To Do column.

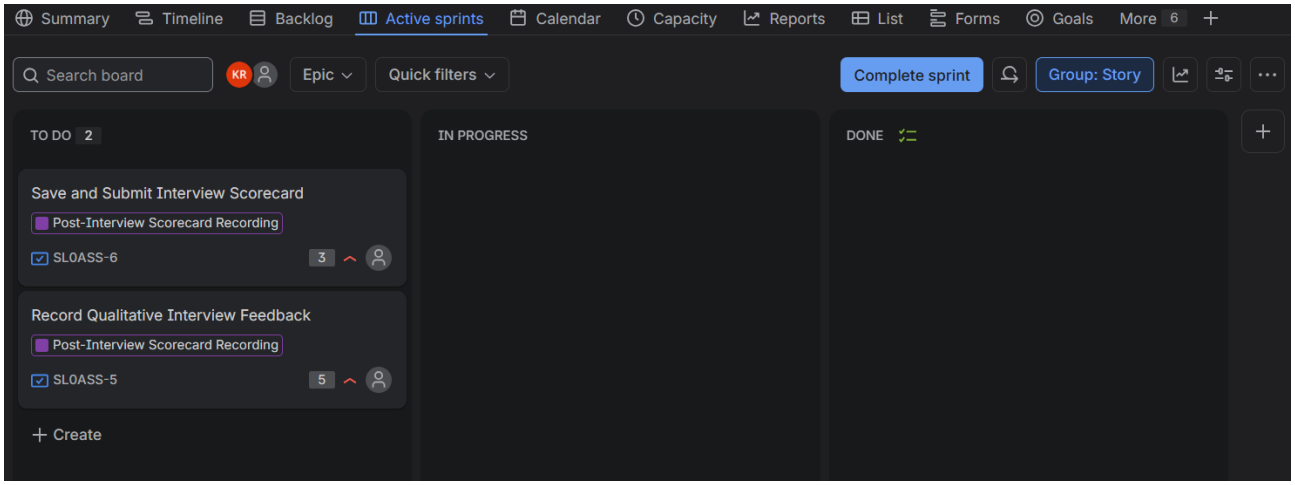


Figure 6. Sprint 2 Active Sprint view at the start of execution.

6. Burndown Chart

The Jira Burndown Chart was configured for SLOASS Sprint 2 using Story Points. Sprint 2 had a planned total of 8 Story Points. The provided visualization shows the remaining Story Points reducing from 8 to 0 as work is completed.

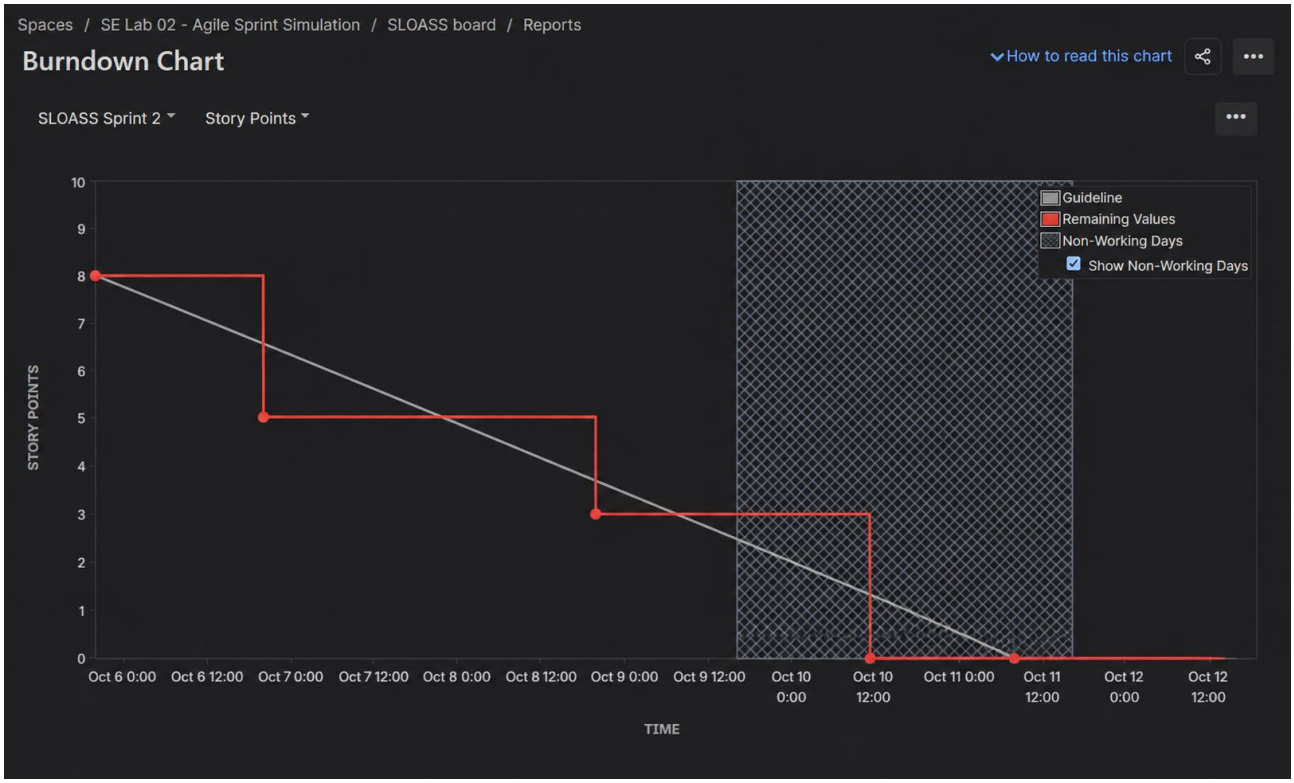


Figure 7. Sprint 2 Burndown Chart configured for Story Points.

7. Reflection

1. What is the purpose of Story Points in Agile?

Story Points provide a relative estimate of the effort, complexity and uncertainty associated with a User Story. They help a Scrum team compare work items and plan realistic sprint scope without treating the estimate as an exact time value.

2. Why is the backlog prioritized?

Prioritization helps the team work on the most valuable or important items first. It also makes sprint planning more systematic because the team can select higher-priority work when deciding what to include in a sprint.

3. What is the role of the Active Sprint board?

The Active Sprint board provides a visual representation of work during the sprint. Moving stories through To Do, In Progress and Done makes the current state of work visible to the team.

4. What does a Burndown Chart indicate?

A Burndown Chart shows how much work remains during a sprint. It can be used to compare actual progress with the expected trend and identify whether the sprint is progressing toward completion.

5. What did you learn from the sprint simulation?

The simulation demonstrated the relationship between backlog refinement, Story Point estimation, sprint planning and execution. It also showed how a Scrum board and burndown report provide visibility into sprint progress.

8. Conclusion

The SE Lab 02 exercise was completed using Jira. The work was organized under an Epic, five User Stories were created and estimated for a total of 19 Story Points, and the work was divided across two sprints of 11 and 8 Story Points. The sprint boards were used to simulate work progression through To Do, In Progress and Done, and the Burndown Chart was reviewed using Story Points.

9. Evidence Note

The figures in this report are the screenshots supplied for the lab work. The Burndown figure is presented as the Story Points visualization associated with the recorded Sprint 2 scope; the Jira screen originally showed the metric selector before it was changed to Story Points.
